


PROJECT OWNER
HABERSHAM COUNTY

ID	Task Mode	Task Name	Duration	Start	Finish	% Complete	2021															
							11/22	Dec	11/29	12/6	12/13	12/20	12/27	Jan	1/3	1/10	1/17	1/24	Feb	1/31	2/7	2/14
1	✓	PRE-CONSTRUCTION MEETING	1 day?	12/2/20	12/2/20	100%																
2	✓	NOTICE TO PROCEED	1 day	12/7/20	12/7/20	100%																
3	✓	EQUIPMENT MOBILIZATION	1 day	12/8/20	12/8/20	100%																
4	✓	INITIAL ENGINEERING & LAYOUT	1 day	12/9/20	12/9/20	100%																
5	✓	CLEARING, & INITIAL EROSION CONTROL	3 days	12/9/20	12/11/20	100%																
6	✓	UTILITY RELOCATION, WINDSTREAM FIBER	2 days	12/14/20	12/15/20	100%																
7		EXCAVATION & EXISTING CULVERT REMOVAL	8 days	12/16/20	12/25/20	90%																
8		DIVERSION, CHANNEL EXCAVATION, & TYPE II BACKFILL	3 days	12/28/20	12/30/20	80%																
9		CAST IN PLACE CULVERT INSTALLATION	30 days	12/31/20	2/10/21	10%																
10		BACKFILL CULVERT, BORROW & UNCLASSIFIED EXCAVATION	10 days	2/11/21	2/24/21	0%																
11		SUB-GRADE PREP, FINISH DRESS, & GRASSING	5 days	2/18/21	2/24/21	0%																
12		GAB PLACEMENT & FINEGRADE	4 days	2/25/21	3/2/21	0%																
13		ASPHALT PAVING	3 days	3/3/21	3/5/21	0%																
14		FINISH DRESS SHOULDERS & GRASSING	1 day?	3/8/21	3/8/21	0%																
15		GAURDRAIL INSTALLATION & STRIPING	2 days	3/9/21	3/10/21	0%																
16		OPEN ROADWAY TO TRAFFIC	1 day	3/11/21	3/11/21	0%																
17		PUNCHLIST AND FINAL CLEAN-UP	2 days	3/11/21	3/12/21	0%																

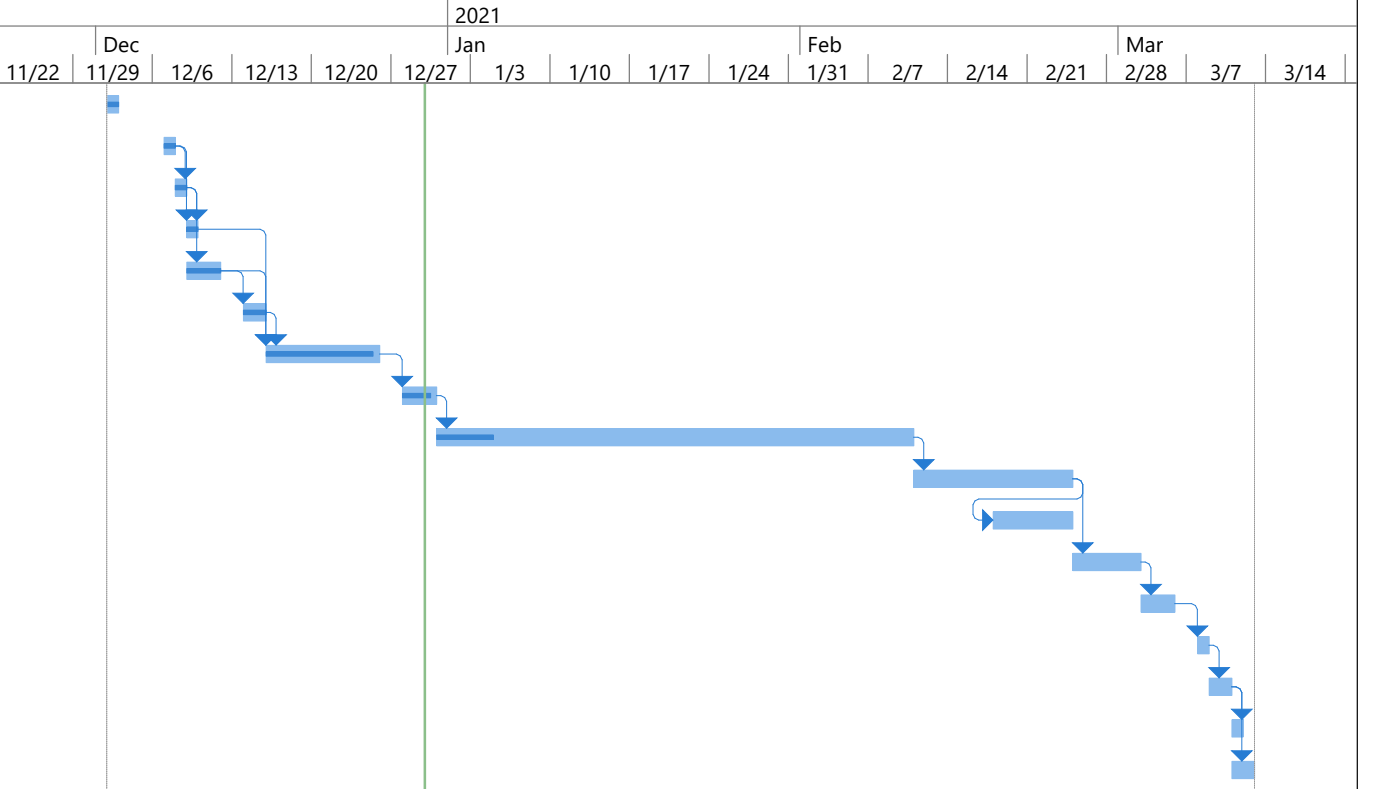

HIGGINS CONSTRUCTION
Project: New Liberty Schedule
Date: 12/30/20

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			
