

TIMELINE

2018 SPLOST VII Project

7,650 Square Feet \$1,750,000.00 **\$228.76**
 Dog Kennels = Qty 45 @ 90sf/kennel = 4,050 sf
 Cat Kennels = Qty 80 @ 45sf/kennel = 3,600 sf
 Total square feet = 7,650

April 2022

Hired Croft for 7,650 Square Foot Building
 Submitting Designers Average Square Foot Price **\$350.00**

March 2023

Add design square footage to approximately 16,000 square feet @ estimated \$350/sf = estimated \$5,600,000



May 2023 – Habersham Animal Control – Schematic Estimate

Axias	Minimal Site	16,427 sf
Total	\$10,050,307.00	\$611.82

July 2023 – Fayette County

Low Bidder	1.27 acres	6,000 sf
Total	\$3,258,357.00	\$543.06

Other Bidders = \$556.15/sf, \$669.66/sf, \$784.82/sf



August 15, 2024 – Sunbelt Builders Preliminary GMP per Plans & Specifications

<u>Habersham Co</u>	<u>10.8 acres</u>	<u>17,513 sf</u>
Site	\$2,351,640.00	\$134.27
Building	\$7,610,966.00	\$434.59
Total	\$9,962,606.00	\$568.86

Habersham County Participation:

Vendors Contacted: 54
 Vendor Bids: 11

Adjacent Area Participation:

Vendors Contacted: 46
 Vendor Bids: 11

Total Participation:

Vendors Contacted: 451
 Vendor Bids: 107



August 22, 2024 – Sunbelt Builders GMP with Value Management Included

<u>Habersham Co</u>	<u>10.8 acers</u>	<u>14,704 sq</u>
Site	\$1,818,682.00	\$123.68
<u>Building</u>	<u>\$5,743,391.00</u>	<u>\$390.60</u>
Total	\$7,562,073.00	\$514.28

Site VE Solutions:




1. Reduce Parking and On-site Drives (\$68,429.00)
2. Reduce Landscaping (\$35,016.00)
3. Subcontractor Buy Out Negotiations (\$58,257.00)
4. Remove Dog Park Lighting (\$24,000.00)
5. Reduce Future Pad & Grading Scope (\$50,000.00)
6. Plan Modifications (1-to-2-month project delay) \$16,000.00


Savings: **(\$219,702.00)**

Habersham County VE Solutions:

1. Haul off / Burning of Trees & Debris *by County* (\$40,000.00)
2. Road to Facility *by County* (\$309,190.00)
3. Asphalt Aggregate provided *by County* (\$37,240.00)
4. Concrete Paving Aggregate provided *by County* (\$1,350.00)
5. Slab on Grade Aggregate by provided *by County* (\$17,645.00)

Savings: **(\$405,425.00)**

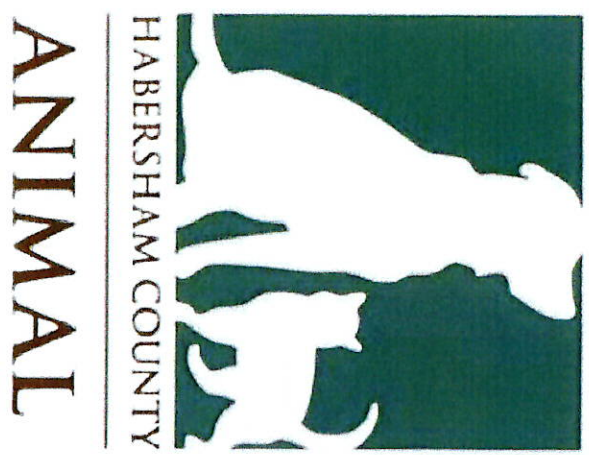



HABERSHAM COUNTY
GEORGIA | Est. 1818



Building VE Solutions:

1. Delete the Generator (\$226,690.00)
2. Delete the Transfer Switch (\$18,577.00)
3. Delete the Incinerator & PE Metal Building (\$218,527.00)
4. Remove Protective Wall Coverings & Corner Guards (\$79,591.00)
5. Reduce Buildings Square Feet (delete Livestock & ½ Sallyport) * (\$935,229.00) *
6. Interior Finish or Equal Products / Scope Change / Low Vendors (\$95,000.00)
7. Mechanical, Electric & Plumbing or Equal Products / Low Vendors (\$110,040.00)
8. Plan Modifications (1-to-2-month project delay) \$64,000.00

Savings: (\$1,619,654.00)

*** (Kennel relocations not accepted by Department)**

Administrative VE Solutions :

1. Delete Construction Contingency (\$50,000.00)
2. Reduced Contractor's Fee (lower GMP) (\$83,446.00)
3. Reduce Bonds & Insurance (lower GMP) (\$22,306.00)


Savings: (\$155,752.00)

VE Solutions NOT included in the above Totals :

1. Change Sloped Roof to Flat Roof (\$418,250.00)
2. Plan Modifications (2-to-3-month project delay) \$55,000.00

Savings: (\$363,250.00)



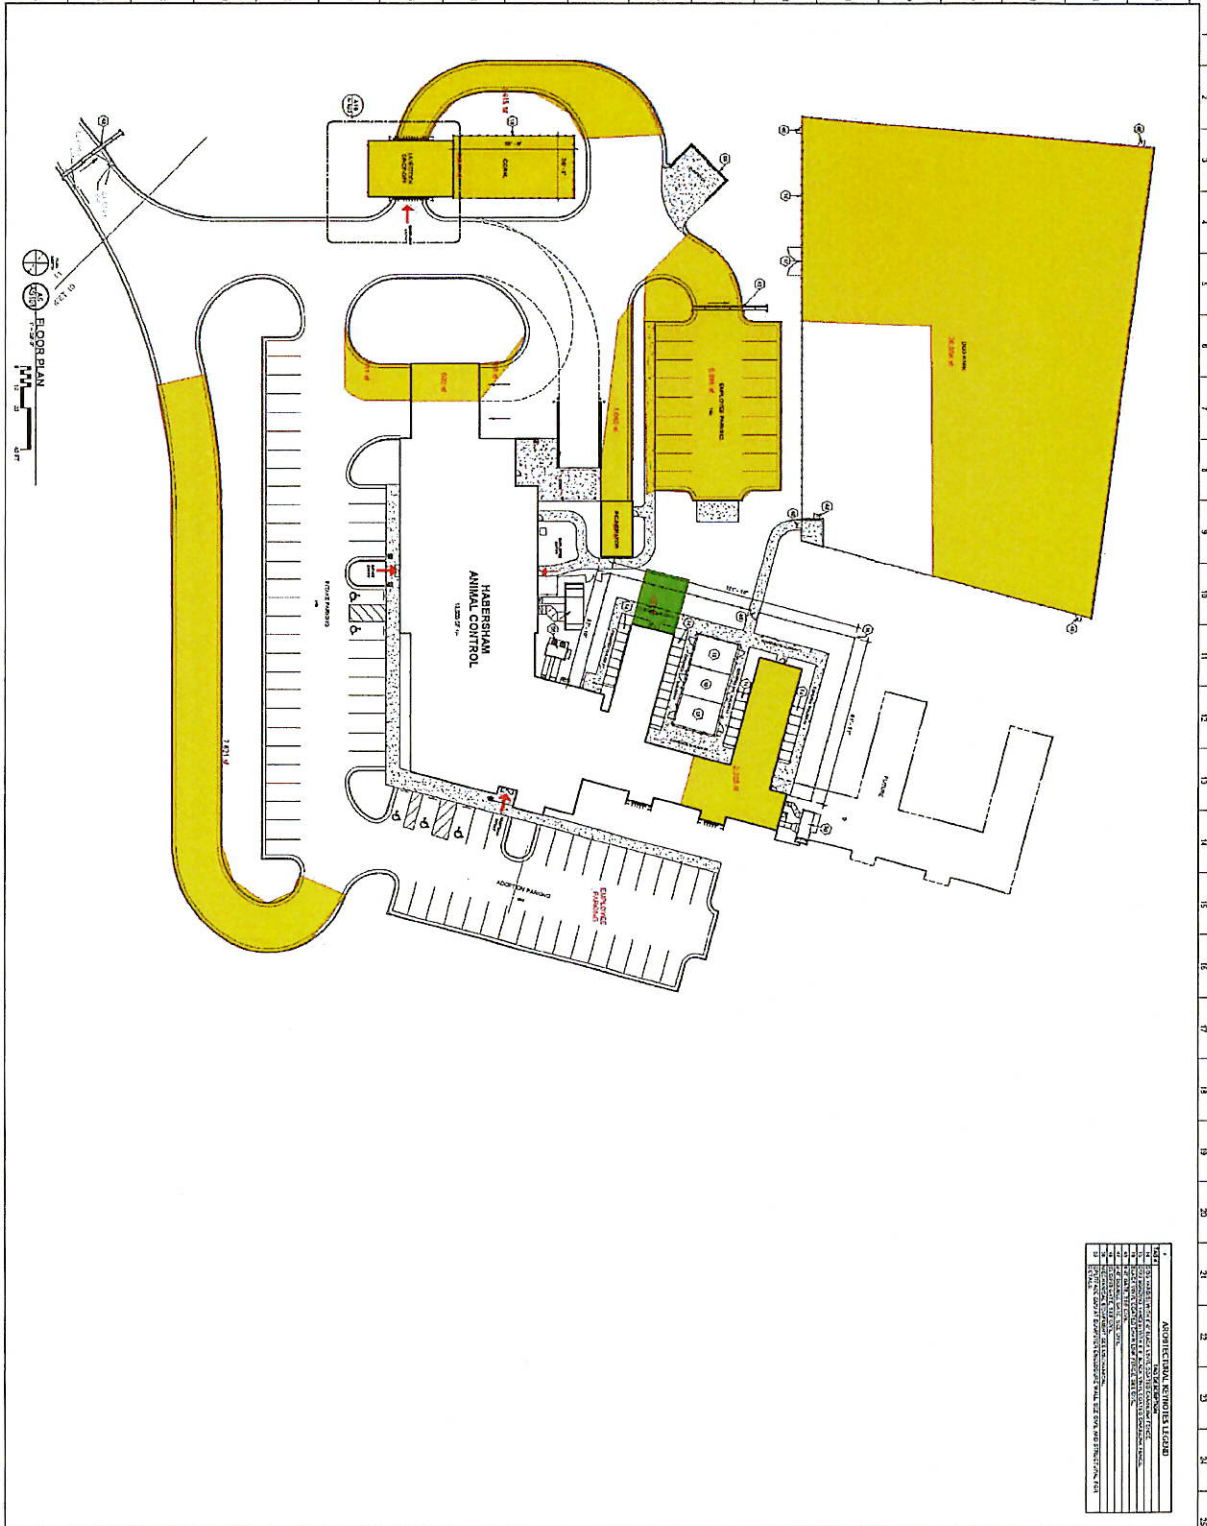

ARCHITECTURAL SYMBOLS LEGEND	
1-1	ASPHALT DRIVE
1-2	CONCRETE DRIVE
1-3	GRAVEL DRIVE
1-4	GRAVEL DRIVE
1-5	GRAVEL DRIVE
1-6	GRAVEL DRIVE
1-7	GRAVEL DRIVE
1-8	GRAVEL DRIVE
1-9	GRAVEL DRIVE
1-10	GRAVEL DRIVE
1-11	GRAVEL DRIVE
1-12	GRAVEL DRIVE
1-13	GRAVEL DRIVE
1-14	GRAVEL DRIVE
1-15	GRAVEL DRIVE
1-16	GRAVEL DRIVE
1-17	GRAVEL DRIVE
1-18	GRAVEL DRIVE
1-19	GRAVEL DRIVE
1-20	GRAVEL DRIVE
1-21	GRAVEL DRIVE
1-22	GRAVEL DRIVE
1-23	GRAVEL DRIVE
1-24	GRAVEL DRIVE
1-25	GRAVEL DRIVE
1-26	GRAVEL DRIVE
1-27	GRAVEL DRIVE
1-28	GRAVEL DRIVE
1-29	GRAVEL DRIVE
1-30	GRAVEL DRIVE
1-31	GRAVEL DRIVE
1-32	GRAVEL DRIVE
1-33	GRAVEL DRIVE
1-34	GRAVEL DRIVE
1-35	GRAVEL DRIVE

CROTTI
Crotti & Associates
Architectural Firm
1000 Peachtree Street, NE
Atlanta, Georgia 30309
Phone: 404.525.1111
Fax: 404.525.1112
www.crotti.com

HABERSHAM ANIMAL SHELTER
HABERSHAM COUNTY ANIMAL CONTROL
COURTNEY
1000 PEACH STREET, NE
ATLANTA, GA 30309
404.525.1111

PROJECT NUMBER: 2024-213
DATE: 06/10/2024
PROJECT: HABERSHAM ANIMAL CONTROL CENTRAL SITE PLAN
DRAWING: AS101



- GENERAL NOTES BY ROOMS:**
1. ROOMS SHOWN IN YELLOW ARE TO BE CONSTRUCTION BY THE CONTRACTOR.
 2. ROOMS SHOWN IN GREEN ARE TO BE CONSTRUCTION BY THE CONTRACTOR.
 3. ROOMS SHOWN IN WHITE ARE TO BE CONSTRUCTION BY THE CONTRACTOR.
 4. ROOMS SHOWN IN WHITE ARE TO BE CONSTRUCTION BY THE CONTRACTOR.
 5. ROOMS SHOWN IN WHITE ARE TO BE CONSTRUCTION BY THE CONTRACTOR.
 6. ROOMS SHOWN IN WHITE ARE TO BE CONSTRUCTION BY THE CONTRACTOR.
 7. ROOMS SHOWN IN WHITE ARE TO BE CONSTRUCTION BY THE CONTRACTOR.
 8. ROOMS SHOWN IN WHITE ARE TO BE CONSTRUCTION BY THE CONTRACTOR.
 9. ROOMS SHOWN IN WHITE ARE TO BE CONSTRUCTION BY THE CONTRACTOR.
 10. ROOMS SHOWN IN WHITE ARE TO BE CONSTRUCTION BY THE CONTRACTOR.
 11. ROOMS SHOWN IN WHITE ARE TO BE CONSTRUCTION BY THE CONTRACTOR.
 12. ROOMS SHOWN IN WHITE ARE TO BE CONSTRUCTION BY THE CONTRACTOR.
 13. ROOMS SHOWN IN WHITE ARE TO BE CONSTRUCTION BY THE CONTRACTOR.
 14. ROOMS SHOWN IN WHITE ARE TO BE CONSTRUCTION BY THE CONTRACTOR.
 15. ROOMS SHOWN IN WHITE ARE TO BE CONSTRUCTION BY THE CONTRACTOR.
 16. ROOMS SHOWN IN WHITE ARE TO BE CONSTRUCTION BY THE CONTRACTOR.
 17. ROOMS SHOWN IN WHITE ARE TO BE CONSTRUCTION BY THE CONTRACTOR.
 18. ROOMS SHOWN IN WHITE ARE TO BE CONSTRUCTION BY THE CONTRACTOR.
 19. ROOMS SHOWN IN WHITE ARE TO BE CONSTRUCTION BY THE CONTRACTOR.
 20. ROOMS SHOWN IN WHITE ARE TO BE CONSTRUCTION BY THE CONTRACTOR.
 21. ROOMS SHOWN IN WHITE ARE TO BE CONSTRUCTION BY THE CONTRACTOR.
 22. ROOMS SHOWN IN WHITE ARE TO BE CONSTRUCTION BY THE CONTRACTOR.
 23. ROOMS SHOWN IN WHITE ARE TO BE CONSTRUCTION BY THE CONTRACTOR.
 24. ROOMS SHOWN IN WHITE ARE TO BE CONSTRUCTION BY THE CONTRACTOR.
 25. ROOMS SHOWN IN WHITE ARE TO BE CONSTRUCTION BY THE CONTRACTOR.
 26. ROOMS SHOWN IN WHITE ARE TO BE CONSTRUCTION BY THE CONTRACTOR.
 27. ROOMS SHOWN IN WHITE ARE TO BE CONSTRUCTION BY THE CONTRACTOR.
 28. ROOMS SHOWN IN WHITE ARE TO BE CONSTRUCTION BY THE CONTRACTOR.
 29. ROOMS SHOWN IN WHITE ARE TO BE CONSTRUCTION BY THE CONTRACTOR.
 30. ROOMS SHOWN IN WHITE ARE TO BE CONSTRUCTION BY THE CONTRACTOR.
 31. ROOMS SHOWN IN WHITE ARE TO BE CONSTRUCTION BY THE CONTRACTOR.
 32. ROOMS SHOWN IN WHITE ARE TO BE CONSTRUCTION BY THE CONTRACTOR.
 33. ROOMS SHOWN IN WHITE ARE TO BE CONSTRUCTION BY THE CONTRACTOR.
 34. ROOMS SHOWN IN WHITE ARE TO BE CONSTRUCTION BY THE CONTRACTOR.

NO.	DESCRIPTION
1	ROOMS SHOWN IN YELLOW ARE TO BE CONSTRUCTION BY THE CONTRACTOR.
2	ROOMS SHOWN IN GREEN ARE TO BE CONSTRUCTION BY THE CONTRACTOR.
3	ROOMS SHOWN IN WHITE ARE TO BE CONSTRUCTION BY THE CONTRACTOR.
4	ROOMS SHOWN IN WHITE ARE TO BE CONSTRUCTION BY THE CONTRACTOR.
5	ROOMS SHOWN IN WHITE ARE TO BE CONSTRUCTION BY THE CONTRACTOR.
6	ROOMS SHOWN IN WHITE ARE TO BE CONSTRUCTION BY THE CONTRACTOR.
7	ROOMS SHOWN IN WHITE ARE TO BE CONSTRUCTION BY THE CONTRACTOR.
8	ROOMS SHOWN IN WHITE ARE TO BE CONSTRUCTION BY THE CONTRACTOR.
9	ROOMS SHOWN IN WHITE ARE TO BE CONSTRUCTION BY THE CONTRACTOR.
10	ROOMS SHOWN IN WHITE ARE TO BE CONSTRUCTION BY THE CONTRACTOR.
11	ROOMS SHOWN IN WHITE ARE TO BE CONSTRUCTION BY THE CONTRACTOR.
12	ROOMS SHOWN IN WHITE ARE TO BE CONSTRUCTION BY THE CONTRACTOR.
13	ROOMS SHOWN IN WHITE ARE TO BE CONSTRUCTION BY THE CONTRACTOR.
14	ROOMS SHOWN IN WHITE ARE TO BE CONSTRUCTION BY THE CONTRACTOR.
15	ROOMS SHOWN IN WHITE ARE TO BE CONSTRUCTION BY THE CONTRACTOR.
16	ROOMS SHOWN IN WHITE ARE TO BE CONSTRUCTION BY THE CONTRACTOR.
17	ROOMS SHOWN IN WHITE ARE TO BE CONSTRUCTION BY THE CONTRACTOR.
18	ROOMS SHOWN IN WHITE ARE TO BE CONSTRUCTION BY THE CONTRACTOR.
19	ROOMS SHOWN IN WHITE ARE TO BE CONSTRUCTION BY THE CONTRACTOR.
20	ROOMS SHOWN IN WHITE ARE TO BE CONSTRUCTION BY THE CONTRACTOR.
21	ROOMS SHOWN IN WHITE ARE TO BE CONSTRUCTION BY THE CONTRACTOR.
22	ROOMS SHOWN IN WHITE ARE TO BE CONSTRUCTION BY THE CONTRACTOR.
23	ROOMS SHOWN IN WHITE ARE TO BE CONSTRUCTION BY THE CONTRACTOR.
24	ROOMS SHOWN IN WHITE ARE TO BE CONSTRUCTION BY THE CONTRACTOR.
25	ROOMS SHOWN IN WHITE ARE TO BE CONSTRUCTION BY THE CONTRACTOR.
26	ROOMS SHOWN IN WHITE ARE TO BE CONSTRUCTION BY THE CONTRACTOR.
27	ROOMS SHOWN IN WHITE ARE TO BE CONSTRUCTION BY THE CONTRACTOR.
28	ROOMS SHOWN IN WHITE ARE TO BE CONSTRUCTION BY THE CONTRACTOR.
29	ROOMS SHOWN IN WHITE ARE TO BE CONSTRUCTION BY THE CONTRACTOR.
30	ROOMS SHOWN IN WHITE ARE TO BE CONSTRUCTION BY THE CONTRACTOR.
31	ROOMS SHOWN IN WHITE ARE TO BE CONSTRUCTION BY THE CONTRACTOR.
32	ROOMS SHOWN IN WHITE ARE TO BE CONSTRUCTION BY THE CONTRACTOR.
33	ROOMS SHOWN IN WHITE ARE TO BE CONSTRUCTION BY THE CONTRACTOR.
34	ROOMS SHOWN IN WHITE ARE TO BE CONSTRUCTION BY THE CONTRACTOR.

PROJECT:
 CROFT ANIMAL SHELTER
 PHASE 2
 FLOOR PLAN
 SHEET NO. A-101

CROFT & ASSOCIATES
 ARCHITECTS
 1000 W. 10TH AVE.
 SUITE 200
 DENVER, CO 80202
 TEL: 303.733.1111
 FAX: 303.733.1112
 WWW.CROFTARCHITECTS.COM

DATE:
 6/19/2024

DESIGNED BY:
 J. HARRIS

DRAWN BY:
 J. HARRIS

CHECKED BY:
 J. HARRIS

APPROVED BY:
 J. HARRIS



CROFT
